


Park Ave Slide Repair and Pave

ID	Task Name	Duration	Start	Finish	Resource Names	8, '19							May 5, '19							May 12, '19						
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S
1	Clearing for Soil Nail	1 day	Tue 4/30/19	Tue 4/30/19	Rohe																					
2	24" Pipe Installation	1 day	Wed 5/8/19	Wed 5/8/19	Rohe																					
3	Excavation for, and Install Soil Nail and Micropiles	21 days	Wed 5/1/19	Wed 5/29/19	GSI and Rohe																					
4	Rip Rap Installation	3 days	Tue 5/28/19	Thu 5/30/19	Rohe																					
5	Excavate Road	3 days	Mon 6/3/19	Wed 6/5/19	Rohe																					
6	Install 53 Base	2 days	Thu 6/6/19	Fri 6/7/19	Rohe																					
7	Pave HMA Base and Surface	2 days	Mon 6/10/19	Tue 6/11/19	Rohe																					

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

Project: Park Ave Slide
Date: Wed 4/24/19

Park Ave Slide Repair and Pave

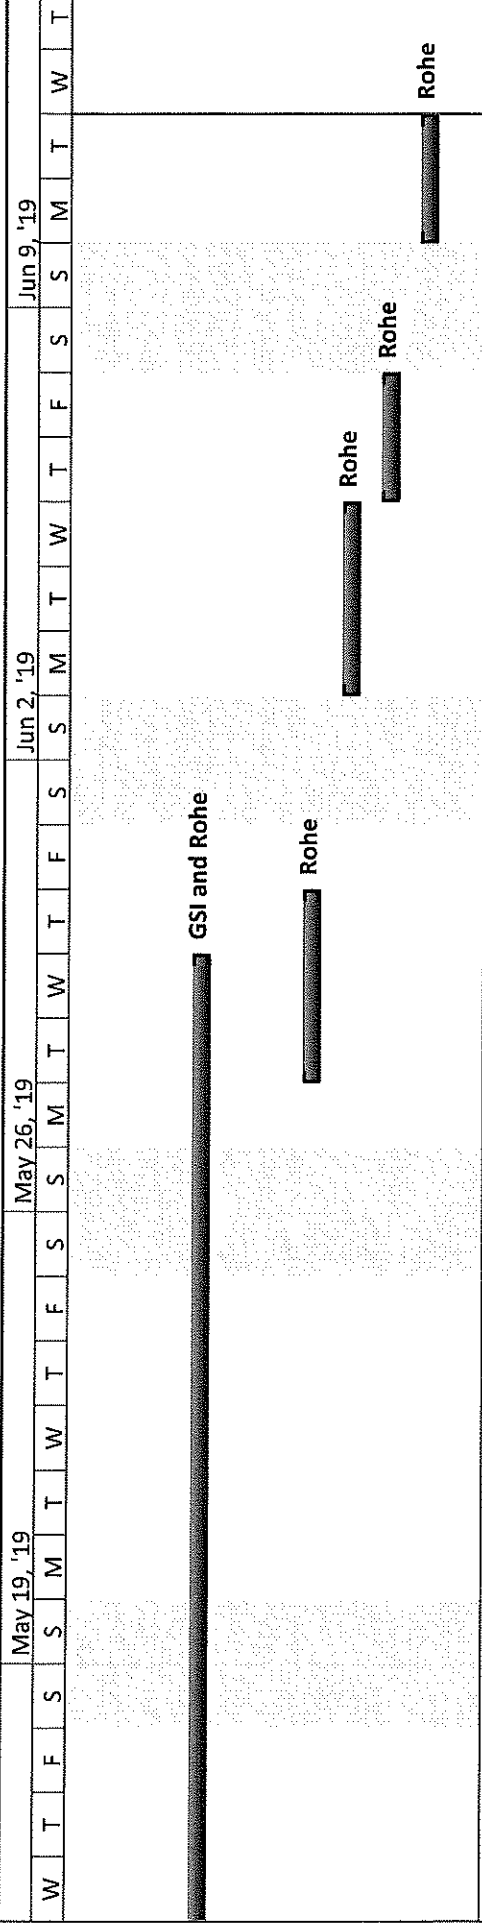

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

Project: Park Ave Slide
Date: Wed 4/24/19
