

Aurora 2nd Street

ID	Task Name	Duration	Start	Finish	May 20, '18							May 27, '18							Jun 3, '18							Jun 10, '18							Jun 17, '18							Jun 24, '18								
					W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T
1	Construction Engineering	3 days	Thu 5/17/18	Mon 5/21/18																																												
2	Construction Signs	1 day	Mon 5/21/18	Mon 5/21/18																																												
3	Install Barrels And Cones	1 day	Tue 5/22/18	Tue 5/22/18																																												
4	Phase 1 North Side Curb and Walk Demo, Pipe and Structure Install	3 days	Wed 5/23/18	Fri 5/25/18																																												
5	Prep for Curbs, Walks, Ramps, and Install Downspout Drains	3 days	Thu 5/24/18	Sat 5/26/18																																												
6	Pour Curbs, Walks, Ramps, Approaches, and Steps	6 days	Fri 5/25/18	Fri 6/1/18																																												
7	HMA Widening	2 days	Mon 6/4/18	Tue 6/5/18																																												
8	Phase 1 South Side Curb and Walk Demo	3 days	Mon 6/4/18	Wed 6/6/18																																												
9	Prep for Curbs, Walks, Ramps, and Install Downspout Drains	3 days	Tue 6/5/18	Thu 6/7/18																																												
10	Pour Curbs, Walks, Ramps, Approaches, and Steps	6 days	Wed 6/6/18	Wed 6/13/18																																												
11	Phase 2 Main St to Mechanic St North Side Curb and Walk Demo	3 days	Thu 6/14/18	Sat 6/16/18																																												
12	Prep for Curbs, Walks, Ramps, and Install Downspout Drains	3 days	Fri 6/15/18	Tue 6/19/18																																												
13	Pour Curbs, Walks, Ramps, Approaches, and Steps	6 days	Mon 6/18/18	Mon 6/25/18																																												
14	Phase 2 Main St to Mechanic St South Side Curb and Walk Demo	3 days	Tue 6/26/18	Thu 6/28/18																																												
15	Prep for Curbs, Walks, Ramps, and Install Downspout Drains	3 days	Wed 6/27/18	Fri 6/29/18																																												
16	Pour Curbs, Walks, Ramps, Approaches, and Steps	7 days	Thu 6/28/18	Fri 7/6/18																																												
17	Phase 3 Mechanic St to Bridgeway North Side Curb and Walk Demo	3 days	Mon 7/9/18	Wed 7/11/18																																												
18	Prep for Curbs, Walks, Ramps, and Install Downspout Drains	3 days	Tue 7/10/18	Thu 7/12/18																																												
19	Pour Curbs, Walks, Ramps, Approaches, and Steps	6 days	Wed 7/11/18	Wed 7/18/18																																												
20	Phase 3 Mechanic St to Bridgeway South Side Curb and Walk Demo	3 days	Thu 7/19/18	Sat 7/21/18																																												
21	Prep for Curbs, Walks, Ramps, and Install Downspout Drains	3 days	Fri 7/20/18	Tue 7/24/18																																												
22	Pour Curbs, Walks, Ramps, Approaches, and Steps	6 days	Mon 7/23/18	Mon 7/30/18																																												

Project: Auror 2nd Street Schedul Date: Fri 5/18/18	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

Aurora 2nd Street

Jul 1, '18				Jul 8, '18				Jul 15, '18				Jul 22, '18				Jul 29, '18				Aug 5, '18				Aug 12, '18				Aug 19, '18				Aug 26, '18																				
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S

Knipenburg

McGraw

McGraw

Knipenburg

McGraw

McGraw

Knipenburg

McGraw


McGraw

Knipenburg

Project: Auror 2nd Street Schedul
Date: Fri 5/18/18

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

Aurora 2nd Street

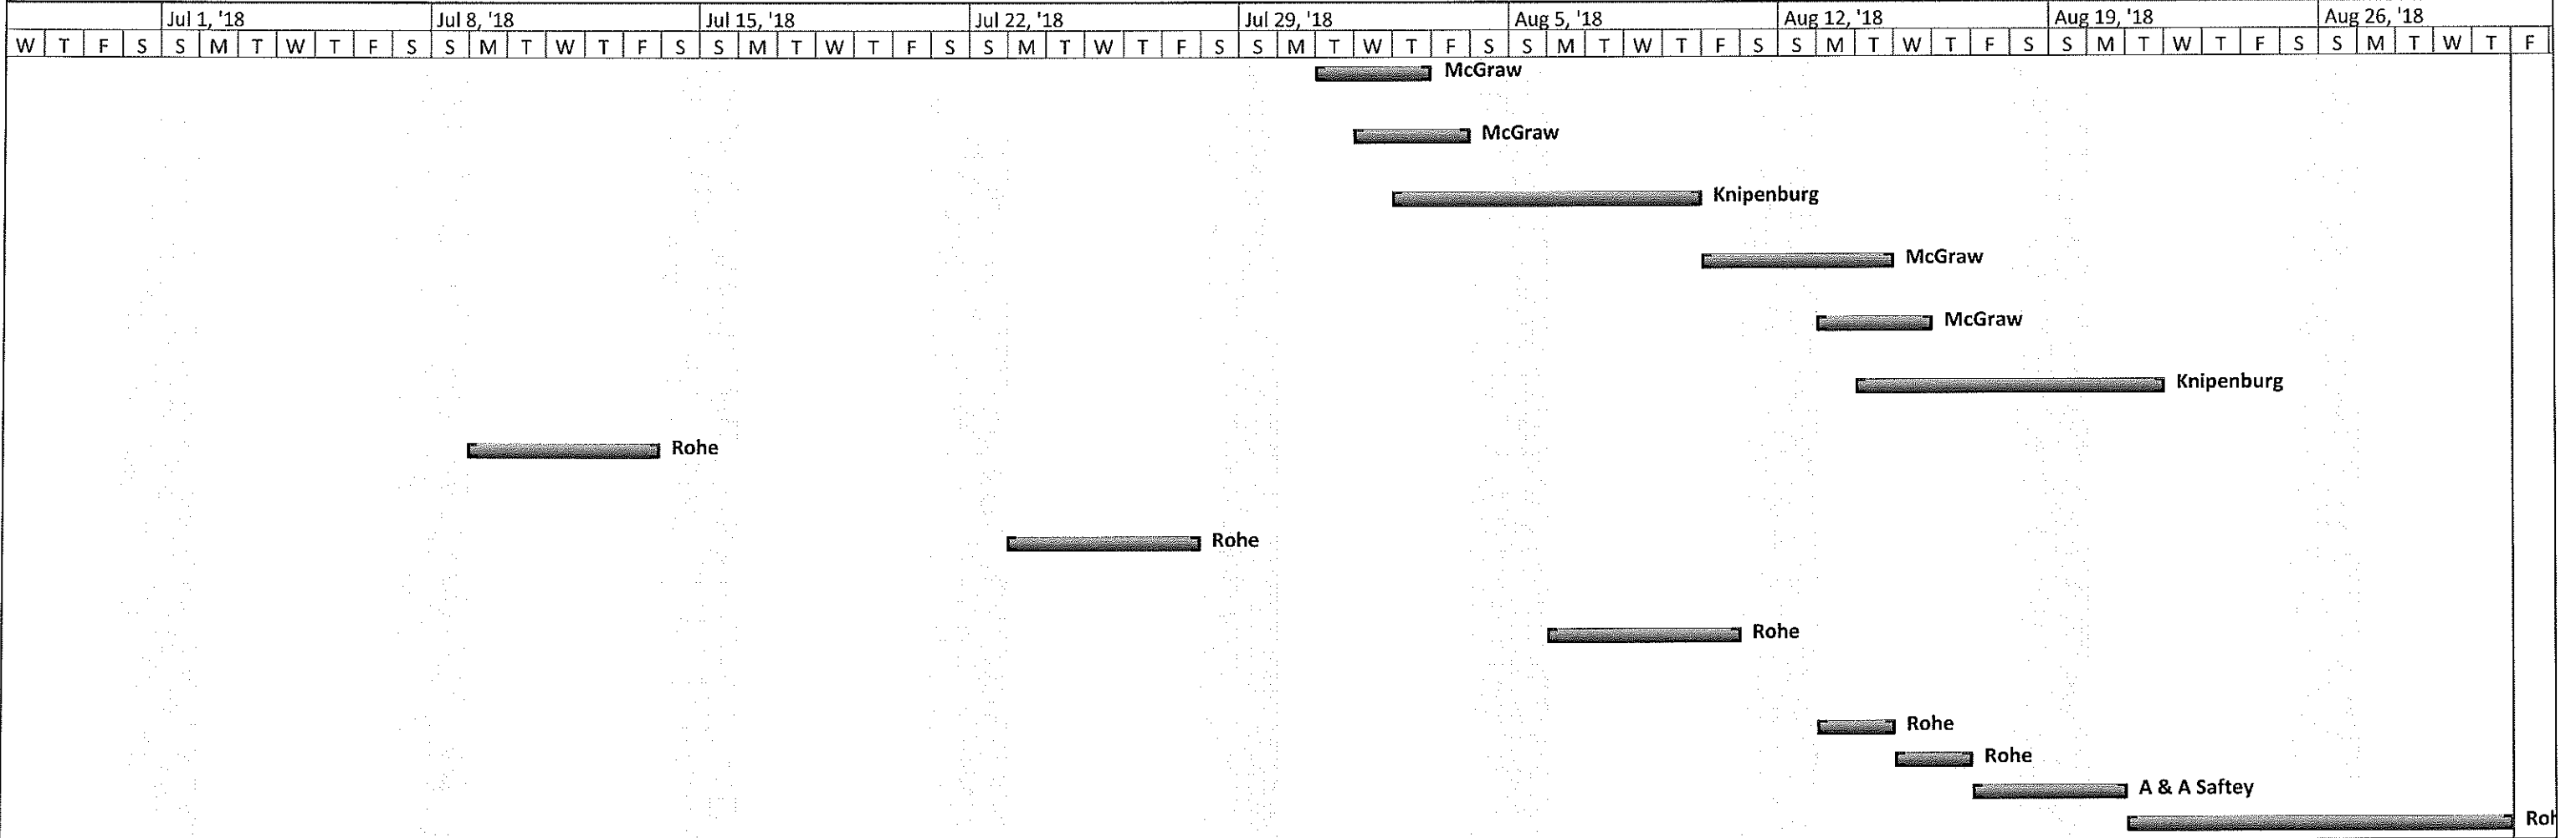

Project: Auror 2nd Street Schedul
Date: Fri 5/18/18

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
